




IATC WEEKLY CONSTRUCTION STATUS UPDATE

INSTITUTE OF APPLIED TECHNOLOGY CONSTRUCTION (IATC)

19th November 2021

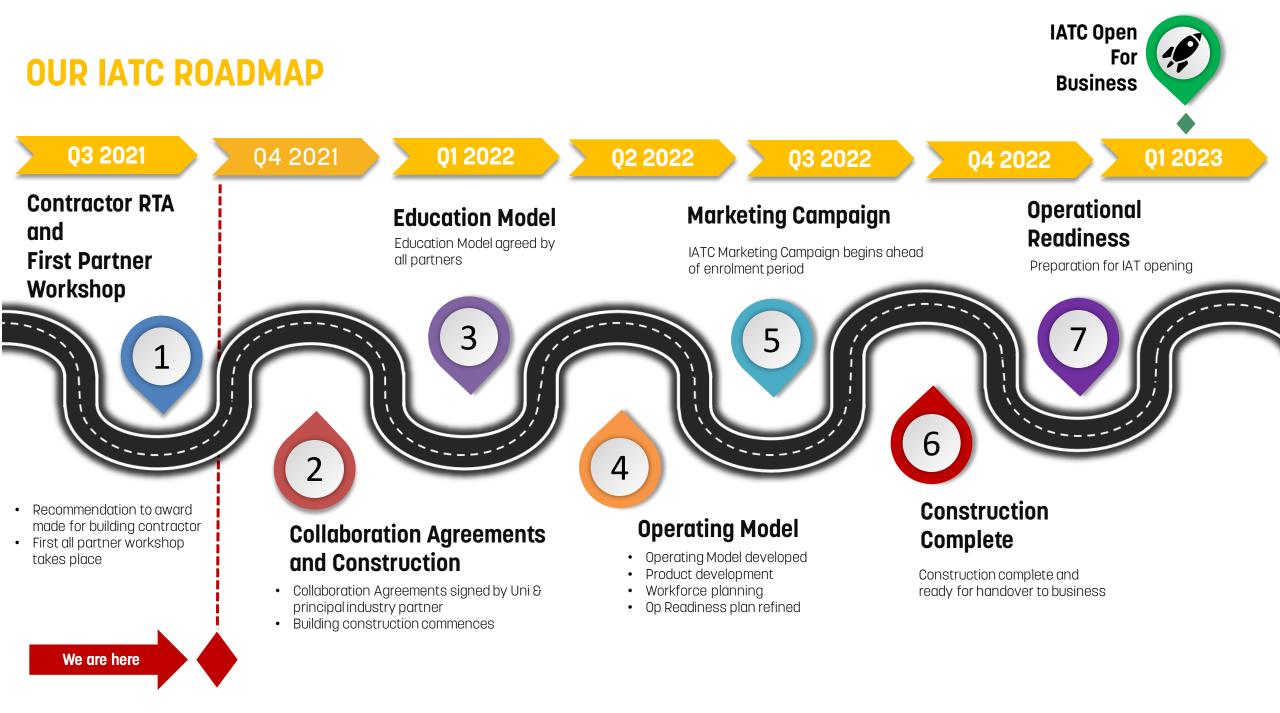

HIGHLIGHTS AND ACHIEVEMENTS (5/11/21-19/11/21)

- Installation of site perimeter fence completed.
- Installation of banner mesh completed.
- Power, water and sewer connections for site accommodation has commenced.
- Civil ground works has commenced onsite.





INSTITUTE OF APPLIED TECHNOLOGY CONSTRUCTION

NEXT STEPS

NOVEMBER

- Construction Traffic Management Plan review and consultation.
- Sediment control installation commences.
- Tree protection and removal program kicks off
- Site clearance commences.
- Removal of site top soil commences.
- Power, Water, Sewer connections to Block T commences.

DECEMBER

- Delivery and establishment of permanent construction site accommodation.
- Excavation and piling site works commence.





PARKING AND TRAFFIC MOVEMENTS (WC 22/11/21)

- Four trucks are scheduled to enter and exit the campus from Tuesday to Thursday through Gate 2 TAFE NSW Nepean-Kingswood.
- Truck movements have been co-ordinated to ensure minimal impact to BAU campus activities.
- The machinery delivered will establish the temporary car park and construction site compound.
- Until temporary construction car parking is established, some construction vehicles may utilise TAFE NSW Nepean- Kingswood car spaces near blocks P and T.

