



IATC WEEKLY CONSTRUCTION STATUS UPDATE

INSTITUTE OF APPLIED TECHNOLOGY CONSTRUCTION (IATC)

15 April 2022

OUR IATC ROADMAP





03 2021

Q4 2021

Q3 2022

Q4 2022

Q1 2023

Contractor RTA and First Partner Workshop

Education Model

Education Model agreed by all partners

Marketing Campaign

IATC Marketing Campaign begins ahead of enrolment period

Operational Readiness

Preparation for IAT opening

 Recommendation to award made for building contractor

• First all partner workshop takes place

Collaboration Agreements and Construction

- Collaboration Agreements signed by Uni & principal industry partner
- Building construction commences

Operating Model

- Operating Model developed
- Product development
- Workforce planning
- Op Readiness plan refined

Construction Complete

Construction complete and ready for handover to business

We are here

HIGHLIGHTS AND ACHIEVEMENTS (WE 16/04/22)

- Wet weather site recovery continued
- Piles and pile caps continued
- Poured concrete to stair 01 walls
- Bulk excavation to northern retaining wall continued
- Formwork and steel reinforcements for lower ground floor columns, lift cores and slab
- Service trenching works commenced from Gate 2
- Crown Development Verification Certificate 2.2 completed and awaiting approval



Service trenching works from Gate 2



SITE PHOTOGRAPHS (WE 16/04/22)



Aerial Drone Photograph



Stair Core 01



Stair Core 01



NEXT STEPS (18/04 - 23/04/22)

APRIL

- Continue wet weather recovery as required
- Continue piling
- reinforcements for lower ground floor columns, lift cores and slab. Major concrete pour targeted late in the week (weather pending)
- *Note: No works scheduled Good Friday
 15/04/2022 and Easter Monday 23/04/2022



Final piling and ground preparation works

COVID 19 MANAGEMENT PLAN

- COVID 19 controls maintained on site
- ADCO and Government Sign in at entry
- SafeWork NSW Management Plans updated
- Awareness signage increased around site
- Scheduled lunch break cycles
- Full time cleaning crew
- Limiting unnecessary site visits
- Project Team Resilience Plan in place







TRAFFIC MOVEMENTS (WC 18/04/22)


Traffic movement through Western Sydney University Werrington South Campus

	Monday 18/04/2022	Tuesday 19/04/2022	Wednesday 20/04/2022	Thursday 21/04/2022	Friday 22/04/2022	Saturday 23/04/2022
Description of Work Activities	EASTER MONDAY	Piling for shoring wall	Piling for shoring wall, formwork to lower ground floor slab and staircore 02 and lift pit		Plastic, pest control, joints and edgeboards for lower ground floor slab	ANZAC LONG WEEKEND
Traffic Control	Nil required	Nil Required	Nil Required	Nil Required	Nil Required	Nil Required
07.00am 08.00am 09.00am 10.00am 11.00am 12.00pm 01.00pm	No work activity on site	Minimal Light Deliveries throughout the day. Nil Traffic Control Required in Place	No planned deliveries	Minimal Light Deliveries throughout the day. Nil Traffic Control Required in Place	No planned deliveries	No work activity on site
03.00pm 04.00pm 05.00pm 06.00pm						



TAFE NSW NEPEAN - KINGSWOOD CAMPUS TRAFFIC PLAN

TAFE NSW Nepean - Kingswood Campus Specific Risk Assessment and Traffic Control Plan

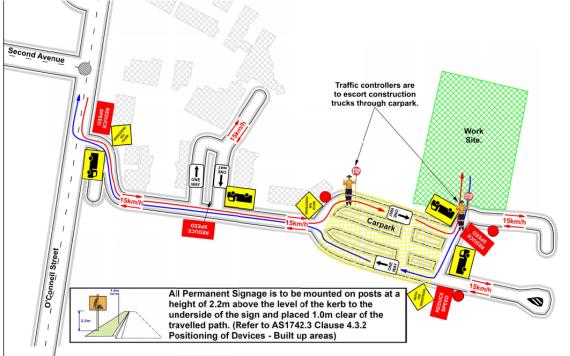





Truck Access Route and Site Plan




CONSTRUCTION TRAFFIC ROUTE AND SITE ACCESS

WESTERN SYDNEY UNIVERSITY WERRIGHTON SOUTH



Blue = Construction traffic entry
Pink = Construction traffic exit

Traffic control will be in place (as required) between:
7am and 6pm Monday-Friday
8am and 1pm Saturdays

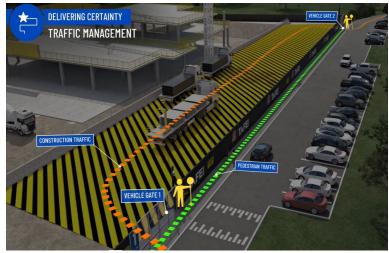

IATC Construction site entry and exit



All construction vehicles with enter and exit the WSU Werrington South Campus in a controlled manner.

All construction vehicle parking will be maintained within the site compound with entry and exit through TAFE NSW Nepean Kingswood Campus.

No WSU parking will be affected due to the construction.



KEY CONTACTS

For key project updates and information about the Institute of Applied Technology for Construction please visit the project website at

IATC project website

Phone: 1800 752 142

Email: iat@tafensw.edu.au

For all project related questions, concerns or complaints please contact:

Cameron Lang, TAFE NSW Investment Project Director at cameron.lang2@tafensw.edu.au or 0408 406 919.

For all day to day construction related question please contact:

Pierce Brennan, ADCO Construction Senior Project Manager on 0419 422 566 Simon Brown, ADCO Construction Site Manager on 0419 012 704 Mitch Alexander, TAFE NSW Senior Project Manager (Cadence Australia) on 0428 440 555

