Institute of Applied Technology
Construction

IAT-C Weekly Construction Status Update

Institute of Applied Technology -Construction (IAT-C) & Multi-Trades 21 July 2023



Context

TAFE NSW is delivering the Institute of Applied Technology - Construction; an \$84.5M Capital investment located at the TAFE NSW Nepean - Kingswood campus.

This new State of the Art, 5 Star Green Star Multitrades facility will provide specialised training in construction, carpentry, electrical and plumbing, to support trades skills shortages in the Western Sydney Region.


The Institute of Applied Technology is a new education offering from the NSW Government, where leading educational institutions and industry will co-locate, co-design, and co-deliver theoretical and practical learning to empower people with the skills and experience they need to thrive in life and work. It will provide employable outcomes, transferrable skills, blended learning, and flexible pathways. This will ensure that NSW has a workforce ready to meet the needs of industry and future infrastructure demand.



Highlights and Achievements (Week ending 22/07/2023)



- Continuation civil high risk area
- Continuation of civil ground works and external landscaped areas, stairs and pathways
- Continuation of services fit-off
- Continuation of external façade, glazing, and soffits
- Continuation of ceiling grids and lighting
- Continuation of painting
- Continuation of floor finishes throughout
- Continuation of joinery installation throughout
- Commencement of large Renlita doors and roller shutter Installation

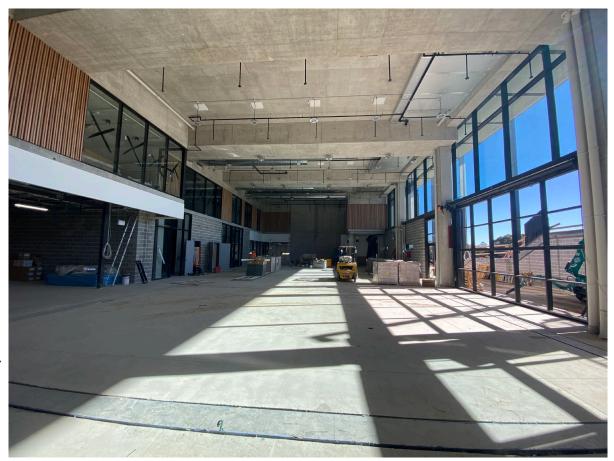


Northern workshop

Site Photograph (Week ending 22/07/2023)





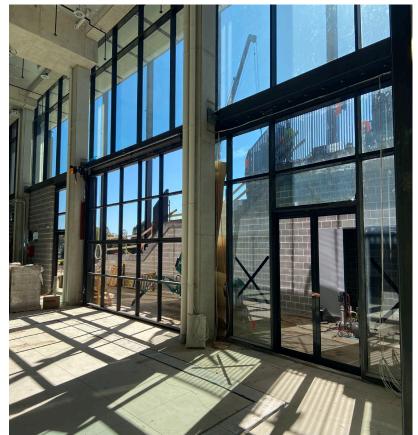

Southern workshop roof and skylights


Tool store window

Northern workshop doors

Institute of Applied Technology Construction

Site Photograph (Week ending 22/07/2023)



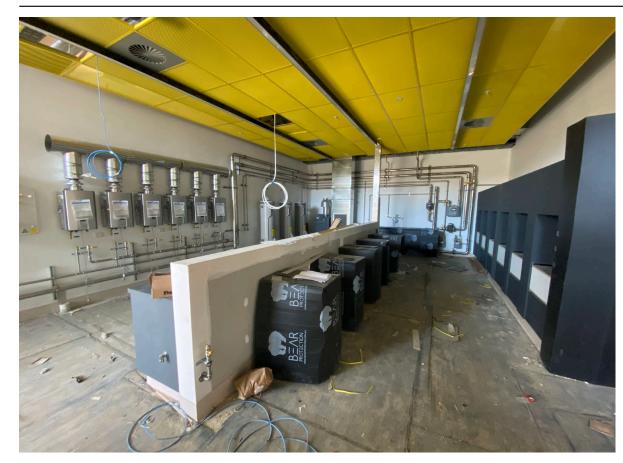



Plumbing gas lab

Café fitout

Institute of Applied Technology Construction

Site Photograph (Week ending 22/07/2023)





Institute of Applied Technology Construction Northern-western aspect

Next Steps (24/07 - 29/07/2023)



- Continuation civil high risk area
- Continuation of civil ground works and external landscaped areas, stairs and pathways
- Continuation of services fit-off
- Continuation of external façade, glazing, and soffits
- Continuation of ceiling grids and lighting
- Continuation of painting
- Continuation of floor finishes throughout
- Continuation of joinery installation throughout
- Continuation of large Renlita doors and roller shutter Installation



Auditorium

Traffic Movements (Week commencing 24/07/2023)



Traffic movement through Western Sydney University Werrington South Campus


Monday	Tuocday	Wodnosday	Thursday	Friday	Saturday						
	•	•	•	· · · · · · · · · · · · · · · · · · ·	29/07/2023						
Fixed RDO	Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout	Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout	Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout	Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout	Continuation of high risk area civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout						
Not required	Not required	Not required	Not required	Not required	Not required						
Deliveries of material expected throughout the day	Deliveries of material expected throughout the day	Deliveries of material expected throughout the day	Deliveries of material expected throughout the day	Deliveries of material expected throughout the day	Deliveries of material expected throughout the day						
							Not required Deliveries of material expected	24/07/2023 Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout Not required Not required Deliveries of material expected Deliveries of material	Tixed RDO Fixed RDO	24/07/2023 Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout Not required Not required Deliveries of material expected Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout Not required Deliveries of material Deliveries of material	24/07/2023 Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout Not required Not required Deliveries of material Continuation of high risk area, civil ground works and external landscaped areas, stairs and pathways, services fit-off, external façade, glazing, soffit linings, ceiling grids, lighting, essential services, painting, floor finishes, and joinery installation throughout Not required Deliveries of material Deliveries of material

Institute of Applied Technology Construction


TAFE NSW Nepean – Kingswood Campus Traffic Plan



TAFE NSW Nepean - Kingswood Campus Specific Risk Assessment and Traffic Control Plan

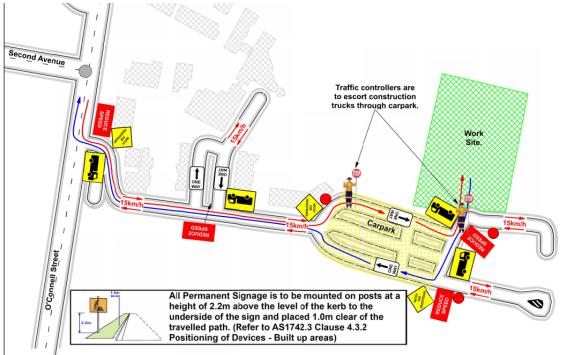



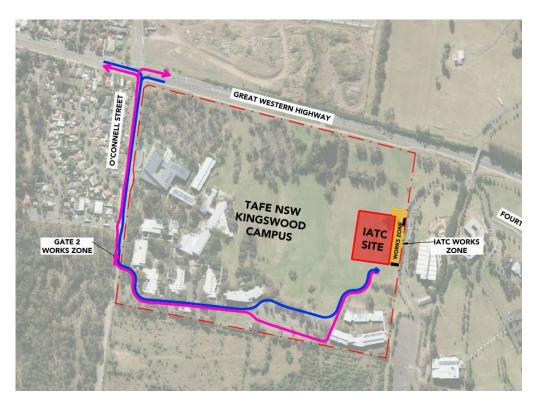

Truck Access Route and Site Plan


Institute of Applied Technology

Construction

TAFE NSW Nepean – Kingswood Campus Traffic Plan




Western Sydney University Werrington South

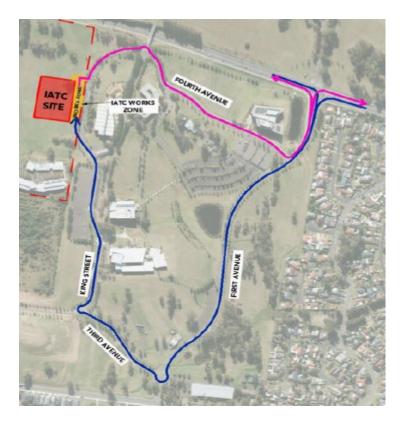

Blue = Construction traffic entry Pink = Construction traffic exit

Traffic control will be in place (as required) between:
7am and 6pm Monday-Friday

8am and 4pm Saturdays

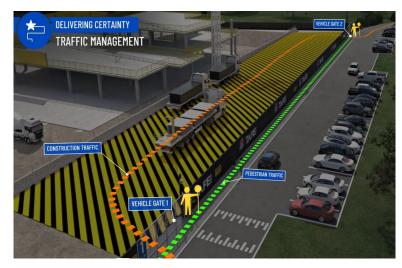

IATC Construction site entry and exit



All construction vehicles with enter and exit the WSU Werrington South Campus in a controlled manner.

All construction vehicle parking will be maintained within the site compound with entry and exit through TAFE NSW Nepean Kingswood Campus.

No WSU parking will be affected due to the construction.

Institute of Applied Technology Construction

Key Contacts



 For key project updates and information about the Institute of Applied Technology - Construction

tafensw.edu.au/instituteofappliedtechnology

Phone: 1800 752 142

■ Email: iat@tafensw.edu.au

For all project related questions, concerns or complaints please contact:

Cameron Lang
TAFE NSW Investment Project Director

Email: cameron.lang2@tafensw.edu.au

Phone: 0408 406 919

For all day to day construction related question please contact:

Pierce Brennan,
ADCO Construction Senior Project Manager

Phone: 0419 422 566

Dion Richards
TAFE NSW Senior Project Manager (Ernst & Young)

Phone: 0423 765 833

Institute of Applied Technology

Construction
